



PlanFlow

PlanFlow V3 Development

Report Generated: 2026-01-14 03:49:01



Project Details

Project Metric	Value
Project Name:	PlanIFlow V3 Development
Start Date:	2026-01-01
End Date:	2026-02-14
Total Tasks:	13
Overall Completion:	43.4%
Currency:	USD
Total Project Cost:	\$27472.00

Task Status Breakdown:

Status	Count
Overdue	0
In Progress	1
Upcoming	4
Completed	4




Task Details

ID	WBS	Task Name	Duration	Start Date	End Date	Dependencies	Resources	%	Status	Notes
1	1	PlanIFlow V3 Project	31.0 days	2026-01-01	2026-02-14	-	-	40%	In Progress	Main project container
2	1.1	Phase 1: Initiation	4.0 days	2026-01-01	2026-01-07	-	-	100%	Completed	-
3	1.1.1	Kickoff Meeting	0 days	2026-01-01	2026-01-01	-	Manager (100%)	100%	Completed	Start of project
4	1.1.2	Gather Requirements	4.0 days	2026-01-02	2026-01-07	3FS	Analyst (100%), Manager (20%)	100%	Completed	Interviews with stakeholders
5	1.2	Phase 2: Development	15.0 days	2026-01-08	2026-01-28	4FS	-	60%	In Progress	-
6	1.2.1	Frontend Architecture	5.0 days	2026-01-08	2026-01-14	-	Senior Dev (100%)	100%	Completed	Choosing framework
7	1.2.2	Backend DB Design	3.0 days	2026-01-08	2026-01-12	-	Backend Dev (100%)	100%	Completed	-
8	1.2.3	Implement API	6.0 days	2026-01-13	2026-01-20	7FS	Backend Dev (100%)	50%	In Progress	Delay expected here
9	1.2.4	Implement UI Components	10.0 days	2026-01-15	2026-01-28	6FS	Junior Dev (100%), Senior Dev (50%)	30%	Upcoming	-
10	1.3	Phase 3: Testing	12.0 days	2026-01-29	2026-02-14	9FS, 8FS	-	0%	Upcoming	-
11	1.3.1	Integration Testing	5.0 days	2026-01-29	2026-02-04	-	Tester (100%)	0%	Upcoming	-
12	1.3.2	Bug Fixes	5.0 days	2026-02-05	2026-02-11	11FS	Senior Dev (100%)	0%	Upcoming	-
13	1.4	Deployment	2.0 days	2026-02-12	2026-02-14	12FS	DevOps (100%)	0%	Upcoming	Go Live!




Gantt Chart (with Critical Path)

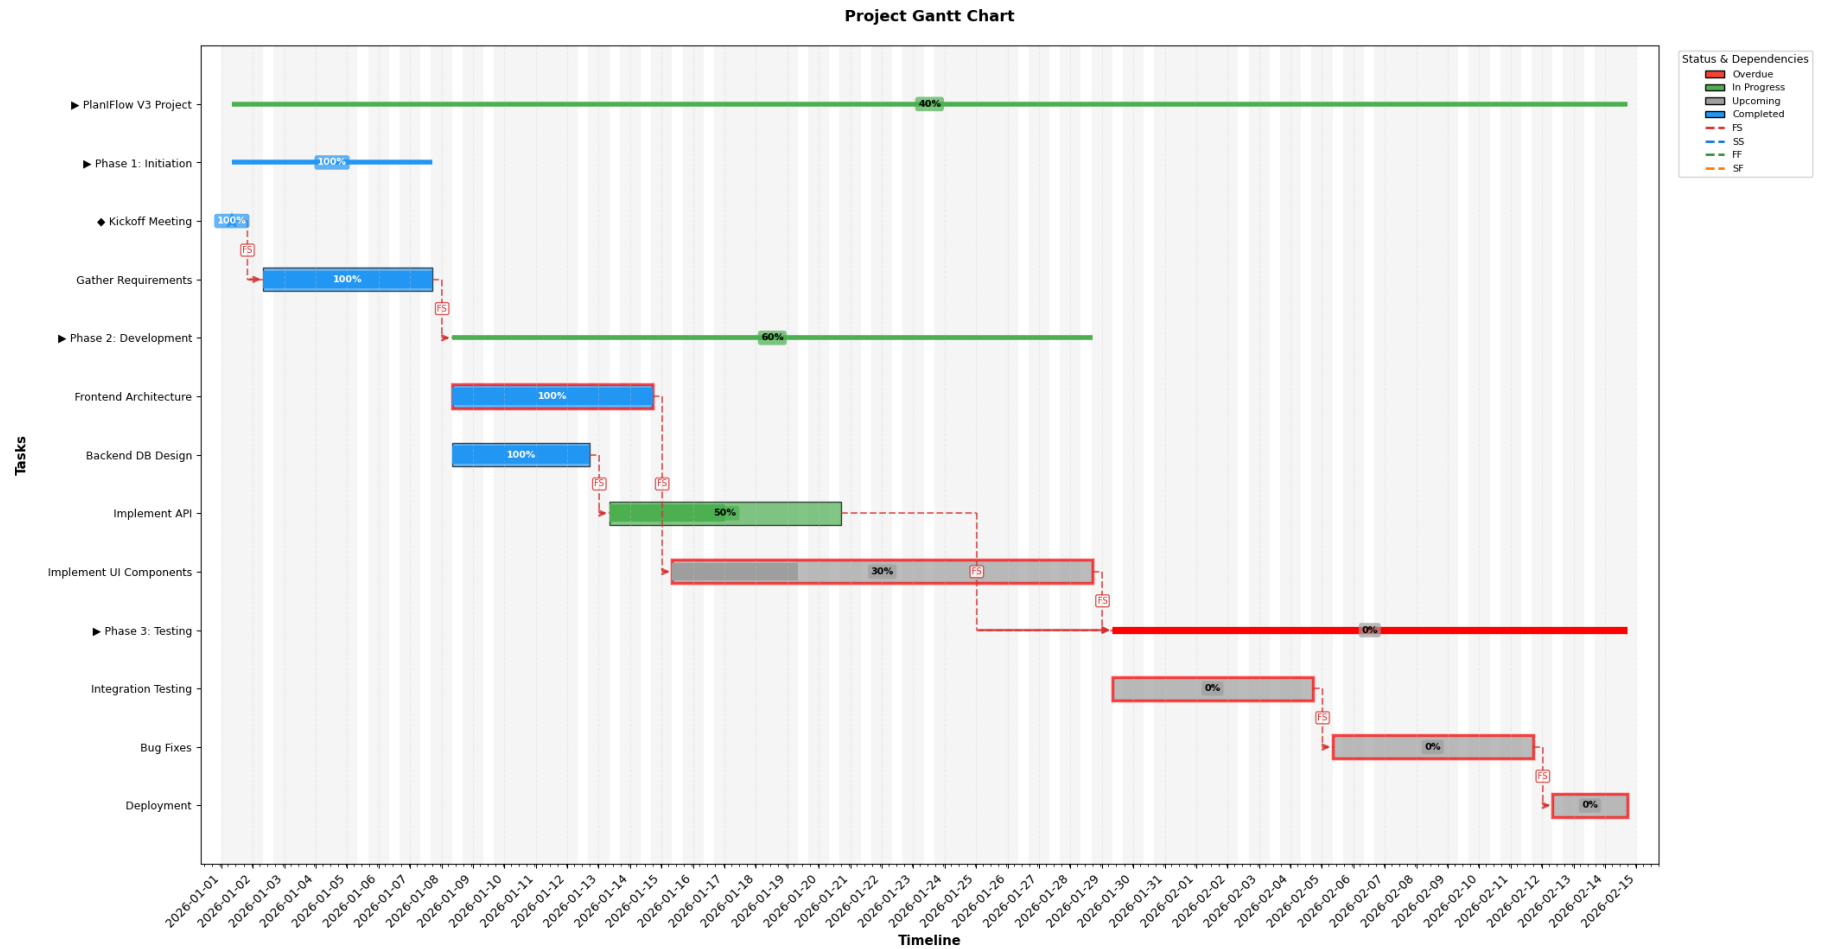



Gantt Chart (without Critical Path)

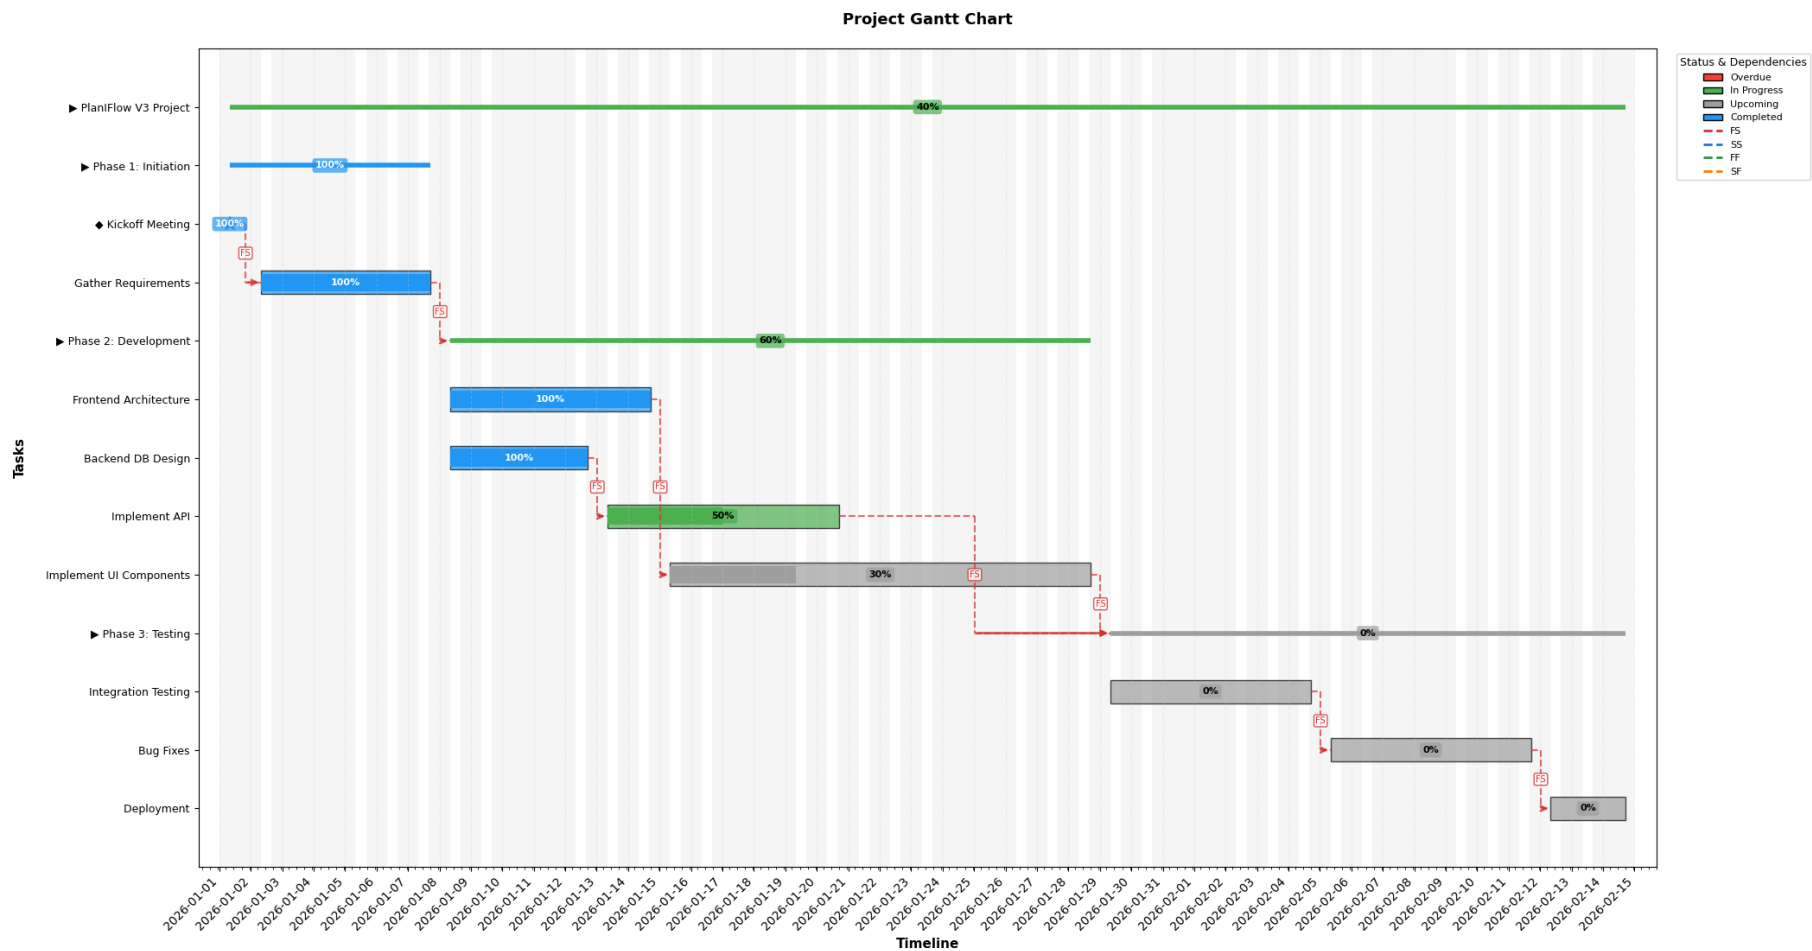



Resource and Cost Details

Resource Name	Max Hours/Day	Billing Rate (\$)	Total Hours Allocated	Total Cost (\$)
Manager	8.0	\$80.00	6.4 hours	\$512.00
Analyst	8.0	\$60.00	32.0 hours	\$1920.00
Senior Dev	8.0	\$100.00	116.0 hours	\$11600.00
Backend Dev	8.0	\$90.00	72.0 hours	\$6480.00
Junior Dev	8.0	\$40.00	80.0 hours	\$3200.00
Tester	8.0	\$50.00	40.0 hours	\$2000.00
DevOps	8.0	\$110.00	16.0 hours	\$1760.00
			Total Project Cost:	\$27472.00



Monthly/Daily Expense Breakdown

Period	Total	Manager	Analyst	Senior Dev	Backend Dev	Junior Dev	Tester	DevOps
Jan-2026	\$20512.00	\$512.00	\$1920.00	\$7600.00	\$6480.00	\$3200.00	\$800.00	\$0.00
Feb-2026	\$6960.00	\$0.00	\$0.00	\$4000.00	\$0.00	\$0.00	\$1200.00	\$1760.00



Project Holidays

The following dates are designated as project-wide non-working days.

Holiday Name	Start Date	End Date	Comment
New Year	2026-01-01	2026-01-01	Happy New Year
